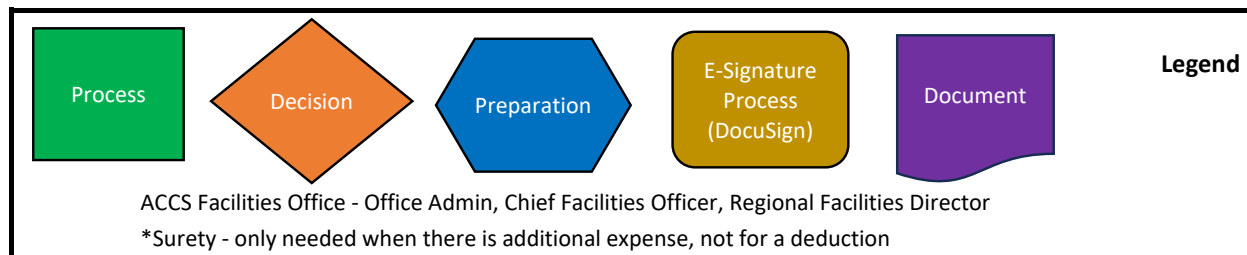
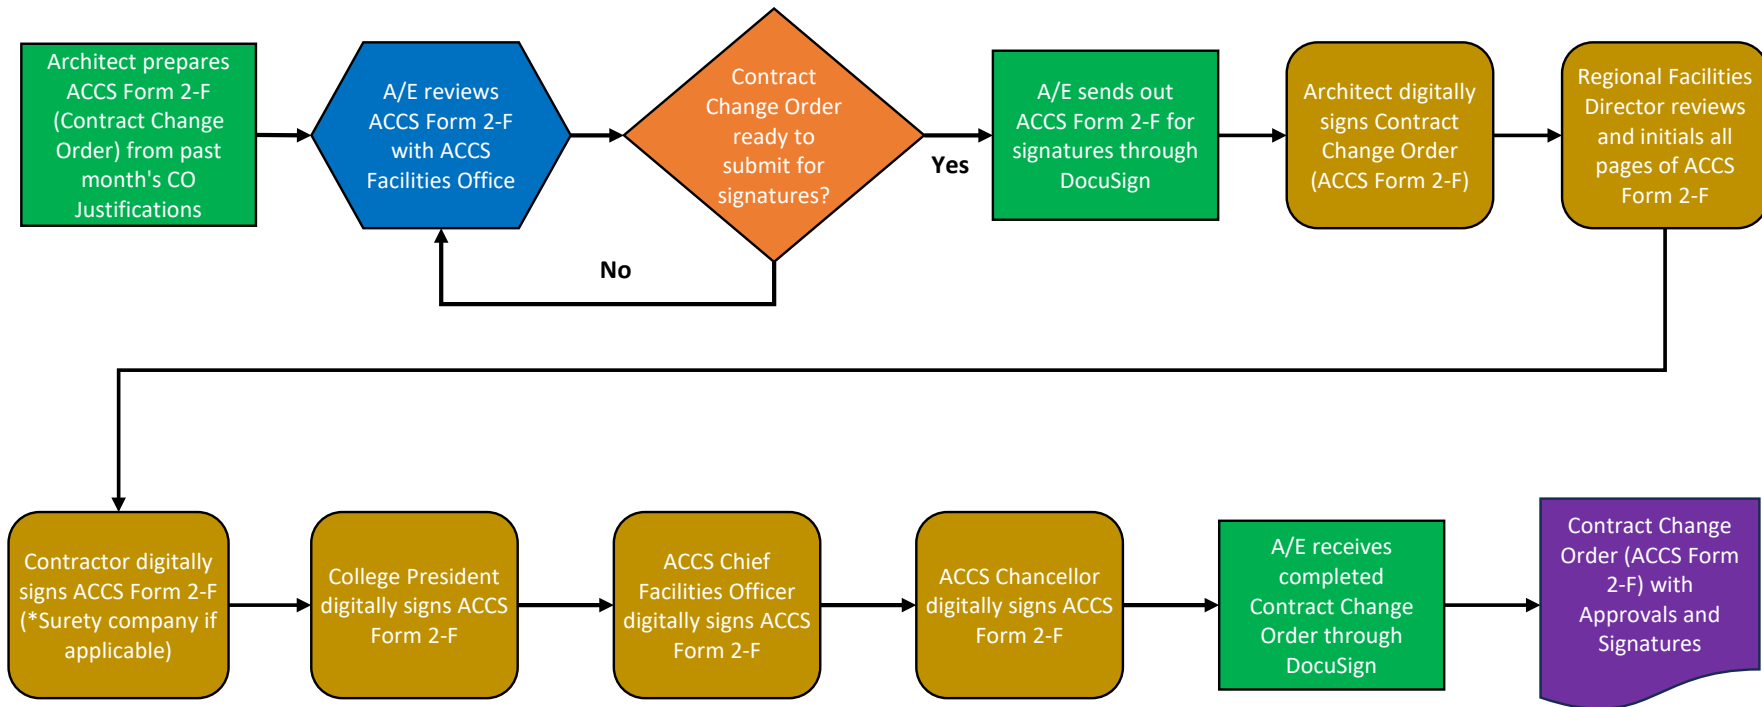


CONTRACT CHANGE ORDER FLOWCHART



ACCS FORM 2-F

ORIGINAL CONTRACT SUM	\$
NET TOTAL OF PREVIOUS CHANGE ORDERS	\$ 0
PREVIOUS REVISED CONTRACT SUM	\$
THIS CHANGE ORDER WILL <input type="radio"/> INCREASE <input type="radio"/> DECREASE	
THE CONTRACT SUM BY	\$
REVISED CONTRACT SUM, INCLUDING THIS CHANGE ORDER	\$
EXTENSION OF TIME RESULTING FROM THIS CHANGE ORDER: <input type="radio"/> NONE or <input type="radio"/> CALENDAR DAYS The amount of this Change Order will be the responsibility of: <Select Client>	

The **OWNER** does hereby certify that this **CHANGE ORDER** was executed per the provisions of Title 39, Code of Alabama, 1975, as amended.

RECOMMENDED BY	CONTRACTING PARTIES
<div>ARCHITECTURAL/ENGINEERING FIRM</div> <div>BY: <input type="text"/></div> <div>NAME: <input type="text"/></div> <div>TITLE: <input type="text"/></div>	<div>CONTRACTOR COMPANY</div> <div>BY: <input type="text"/></div> <div>NAME: <input type="text"/></div> <div>TITLE: <input type="text"/></div>
<div>COMMUNITY COLLEGE PRESIDENT</div> <div>BY: <input type="text"/></div> <div>SIGNATURE OF OFFICER</div> <div>NAME: <input type="text"/></div> <div>TITLE: <input type="text"/></div>	<div>ALABAMA COMMUNITY COLLEGE SYSTEM (AS OWNER)</div> <div>BY: <input type="text"/></div> <div>CHANCELLOR</div>
<div>ALABAMA COMMUNITY COLLEGE SYSTEM (ACCS)</div> <div>BY: <input type="text"/> DATE: <input type="text"/></div> <div>CHIEF FACILITIES OFFICER</div>	<div>CONSENT OF SURETY</div> <div>SURETY COMPANY</div> <div>BY: <input type="text"/></div> <div>(ATTACH CURRENT POWER OF ATTORNEY)</div>

Review/Initial of Regional Facilities Director

VER: 04252024



FACILITIES DIVISION

ACCS FORM 2-F

***NOTE:** Any Change Orders without documented ACCS Facilities Division approval will be at the expense of the Architect and/or the Contractor.

CONTRACT CHANGE ORDER

ACCS PROJECT#:	
CHANGE ORDER#:	
DATE:	
PROJECT: 	
TO: <input type="text"/>	
Address:	<input type="text"/>
<p>TERMS: You are hereby authorized, subject to the provisions of your Contract for this project, to make the following changes thereto in accordance with your proposal(s) dated: <input type="text"/></p> <p>FURNISH the necessary labor, materials, and equipment to: (Description of work to be done or changes to be made. If the description is continued in an attachment, identify the attachment below.)</p> <div style="border: 1px solid black; height: 150px; width: 100%;"></div>	

2

Review/Initial of Regional Facilities Director

VER: 04252024

ACCS FORM 2-F

ORIGINAL CONTRACT SUM	\$
NET TOTAL OF PREVIOUS CHANGE ORDERS	\$ 0
PREVIOUS REVISED CONTRACT SUM	\$
THIS CHANGE ORDER WILL <input type="radio"/> INCREASE <input type="radio"/> DECREASE	
THE CONTRACT SUM BY	\$
REVISED CONTRACT SUM, INCLUDING THIS CHANGE ORDER	\$
EXTENSION OF TIME RESULTING FROM THIS CHANGE ORDER: <input type="radio"/> NONE or <input type="radio"/> CALENDAR DAYS The amount of this Change Order will be the responsibility of: <Select Client>	


The **OWNER** does hereby certify that this **CHANGE ORDER** was executed per the provisions of Title 39, Code of Alabama, 1975, as amended.

RECOMMENDED BY	CONTRACTING PARTIES
<div>ARCHITECTURAL/ENGINEERING FIRM</div> <div>BY: <input type="text"/></div> <div>NAME: <input type="text"/></div> <div>TITLE: <input type="text"/></div>	<div>CONTRACTOR COMPANY</div> <div>BY: <input type="text"/></div> <div>NAME: <input type="text"/></div> <div>TITLE: <input type="text"/></div>
<div>APPROVALS</div> <div>COMMUNITY COLLEGE PRESIDENT</div> <div>BY: <input type="text"/></div> <div>SIGNATURE OF OFFICER</div> <div>NAME: <input type="text"/></div> <div>TITLE: <input type="text"/></div>	<div>ALABAMA COMMUNITY COLLEGE SYSTEM (AS OWNER)</div> <div>BY: <input type="text"/></div> <div>CHANCELLOR</div>
<div>ALABAMA COMMUNITY COLLEGE SYSTEM (ACCS)</div> <div>BY: <input type="text"/> DATE: <input type="text"/></div> <div>CHIEF FACILITIES OFFICER</div>	<div>CONSENT OF SURETY</div> <div>SURETY COMPANY</div> <div>BY: <input type="text"/></div> <div>(ATTACH CURRENT POWER OF ATTORNEY)</div>














2Review/Initial of Regional Facilities Director

VER: 04252024

ACCS FORM 2-F

ORIGINAL CONTRACT SUM	\$
NET TOTAL OF PREVIOUS CHANGE ORDERS	\$0
PREVIOUS REVISED CONTRACT SUM	\$
THIS CHANGE ORDER WILL <input type="radio"/> INCREASE <input type="radio"/> DECREASE	
THE CONTRACT SUM BY	\$
REVISED CONTRACT SUM, INCLUDING THIS CHANGE ORDER	\$
EXTENSION OF TIME RESULTING FROM THIS CHANGE ORDER: <input type="radio"/> NONE or <input type="radio"/> CALENDAR DAYS The amount of this Change Order will be the responsibility of: <Select Client> 	


The **OWNER** does hereby certify that this **CHANGE ORDER** was executed per the provisions of Title 39, Code of Alabama, 1975, as amended.

RECOMMENDED BY	CONTRACTING PARTIES 3
<div>ARCHITECTURAL/ENGINEERING FIRM</div> <div>BY: </div> <div>NAME: </div> <div>TITLE: </div>	<div>CONTRACTOR COMPANY</div> <div>BY: </div> <div>NAME: </div> <div>TITLE: </div>
<div>APPROVALS</div> <div>COMMUNITY COLLEGE PRESIDENT</div> <div>BY: </div> <div>SIGNATURE OF OFFICER</div> <div>NAME: </div> <div>TITLE: </div> <div>ALABAMA COMMUNITY COLLEGE SYSTEM (ACCS)</div> <div>BY:  DATE: </div> <div>CHIEF FACILITIES OFFICER</div>	<div>ALABAMA COMMUNITY COLLEGE SYSTEM (AS OWNER)</div> <div>BY: </div> <div>CHANCELLOR</div> <div>CONSENT OF SURETY</div> <div>SURETY COMPANY</div> <div>BY: </div> <div>(ATTACH CURRENT POWER OF ATTORNEY)</div>














Review/Initial of Regional Facilities Director 

VER: 04252024

ACCS FORM 2-F

ORIGINAL CONTRACT SUM	\$
NET TOTAL OF PREVIOUS CHANGE ORDERS	\$0
PREVIOUS REVISED CONTRACT SUM	\$
THIS CHANGE ORDER WILL <input type="radio"/> INCREASE <input type="radio"/> DECREASE	
THE CONTRACT SUM BY	\$
REVISED CONTRACT SUM, INCLUDING THIS CHANGE ORDER	\$
EXTENSION OF TIME RESULTING FROM THIS CHANGE ORDER: <input type="radio"/> NONE or <input type="radio"/> CALENDAR DAYS The amount of this Change Order will be the responsibility of: <Select Client> 	


The **OWNER** does hereby certify that this **CHANGE ORDER** was executed per the provisions of Title 39, Code of Alabama, 1975, as amended.

RECOMMENDED BY	CONTRACTING PARTIES
<div>ARCHITECTURAL/ENGINEERING FIRM</div> <div>BY: </div> <div>NAME: </div> <div>TITLE: </div>	<div>CONTRACTOR COMPANY</div> <div>BY: </div> <div>NAME: </div> <div>TITLE: </div>
<div>APPROVALS</div> <div><div>COMMUNITY COLLEGE PRESIDENT</div><div>BY: </div><div>SIGNATURE OF OFFICER</div><div>NAME: </div><div>TITLE: </div></div> <div><div>ALABAMA COMMUNITY COLLEGE SYSTEM (ACCS)</div><div>BY:  DATE: </div><div>CHIEF FACILITIES OFFICER</div></div>	<div>ALABAMA COMMUNITY COLLEGE SYSTEM (AS OWNER)</div> <div>BY: </div> <div>CHANCELLOR</div>
	<div>4</div> <div>CONSENT OF SURETY</div> <div><div>SURETY COMPANY</div><div>BY: </div><div>(ATTACH CURRENT POWER OF ATTORNEY)</div></div>







Review/Initial of Regional Facilities Director 

VER: 04252024

ACCS FORM 2-F

ORIGINAL CONTRACT SUM	\$
NET TOTAL OF PREVIOUS CHANGE ORDERS	\$0
PREVIOUS REVISED CONTRACT SUM	\$
THIS CHANGE ORDER WILL <input type="radio"/> INCREASE <input type="radio"/> DECREASE	
THE CONTRACT SUM BY	\$
REVISED CONTRACT SUM, INCLUDING THIS CHANGE ORDER	\$
EXTENSION OF TIME RESULTING FROM THIS CHANGE ORDER: <input type="radio"/> NONE or <input type="radio"/> CALENDAR DAYS The amount of this Change Order will be the responsibility of: <Select Client> 	

The **OWNER** does hereby certify that this **CHANGE ORDER** was executed per the provisions of Title 39, Code of Alabama, 1975, as amended.

RECOMMENDED BY	CONTRACTING PARTIES
<div><div></div><div>ARCHITECTURAL/ENGINEERING FIRM</div><div>BY: </div><div>NAME: <div></div></div><div>TITLE: <div></div></div></div>	<div><div></div><div>CONTRACTOR COMPANY</div><div>BY: </div><div>NAME: <div></div></div><div>TITLE: <div></div></div></div>
<div><div>APPROVALS</div><div><div></div><div>COMMUNITY COLLEGE PRESIDENT</div><div>BY: </div><div>SIGNATURE OF OFFICER</div><div>NAME: <div></div></div><div>TITLE: <div></div></div></div></div>	<div><div>ALABAMA COMMUNITY COLLEGE SYSTEM (AS OWNER)</div><div>BY: </div><div>CHANCELLOR</div></div>
<div><div>ALABAMA COMMUNITY COLLEGE SYSTEM (ACCS)</div><div>BY: </div><div>CHIEF FACILITIES OFFICER</div><div>DATE: <div></div></div></div>	<div><div>CONSENT OF SURETY</div><div><div></div><div>SURETY COMPANY</div><div>BY: </div><div>(ATTACH CURRENT POWER OF ATTORNEY)</div></div></div>

Review/Initial of Regional Facilities Director

VER: 04252024

ACCS FORM 2-F

ORIGINAL CONTRACT SUM	\$
NET TOTAL OF PREVIOUS CHANGE ORDERS	\$0
PREVIOUS REVISED CONTRACT SUM	\$
THIS CHANGE ORDER WILL <input type="radio"/> INCREASE <input type="radio"/> DECREASE	
THE CONTRACT SUM BY	\$
REVISED CONTRACT SUM, INCLUDING THIS CHANGE ORDER	\$
EXTENSION OF TIME RESULTING FROM THIS CHANGE ORDER: <input type="radio"/> NONE or <input type="radio"/> CALENDAR DAYS The amount of this Change Order will be the responsibility of: <Select Client>	


The **OWNER** does hereby certify that this **CHANGE ORDER** was executed per the provisions of Title 39, Code of Alabama, 1975, as amended.

RECOMMENDED BY ARCHITECTURAL/ENGINEERING FIRM BY: NAME: TITLE:	CONTRACTING PARTIES CONTRACTOR COMPANY BY: NAME: TITLE: ALABAMA COMMUNITY COLLEGE SYSTEM (AS OWNER) BY: CHANCELLOR
APPROVALS COMMUNITY COLLEGE PRESIDENT BY: SIGNATURE OF OFFICER NAME: TITLE:	CONSENT OF SURETY SURETY COMPANY BY: (ATTACH CURRENT POWER OF ATTORNEY)
ALABAMA COMMUNITY COLLEGE SYSTEM (ACCS) BY: CHIEF FACILITIES OFFICER DATE:	














Review/Initial of Regional Facilities Director

VER: 04252024

ACCS FORM 2-F

ORIGINAL CONTRACT SUM	\$
NET TOTAL OF PREVIOUS CHANGE ORDERS	\$0
PREVIOUS REVISED CONTRACT SUM	\$
THIS CHANGE ORDER WILL <input type="radio"/> INCREASE <input type="radio"/> DECREASE	
THE CONTRACT SUM BY	\$
REVISED CONTRACT SUM, INCLUDING THIS CHANGE ORDER	\$
EXTENSION OF TIME RESULTING FROM THIS CHANGE ORDER: <input type="radio"/> NONE or <input type="radio"/> CALENDAR DAYS The amount of this Change Order will be the responsibility of: <Select Client> 	

The **OWNER** does hereby certify that this **CHANGE ORDER** was executed per the provisions of Title 39, Code of Alabama, 1975, as amended.

RECOMMENDED BY	CONTRACTING PARTIES
<div>ARCHITECTURAL/ENGINEERING FIRM</div> <div>BY: </div> <div>NAME: </div> <div>TITLE: </div>	<div>CONTRACTOR COMPANY</div> <div>BY: </div> <div>NAME: </div> <div>TITLE: </div>
<div>APPROVALS</div> <div>COMMUNITY COLLEGE PRESIDENT</div> <div>BY: </div> <div>SIGNATURE OF OFFICER</div> <div>NAME: </div> <div>TITLE: </div> <div>ALABAMA COMMUNITY COLLEGE SYSTEM (ACCS)</div> <div>BY:  DATE: </div> <div>CHIEF FACILITIES OFFICER</div>	<div>ALABAMA COMMUNITY COLLEGE SYSTEM (AS OWNER)</div> <div>BY: </div> <div>CHANCELLOR</div> <div>7</div> <div>CONSENT OF SURETY</div> <div>SURETY COMPANY</div> <div>BY: </div> <div>(ATTACH CURRENT POWER OF ATTORNEY)</div>

Review/Initial of Regional Facilities Director 

VER: 04252024
